

Programme

August 2025

The East Midlands Gateway Phase 2
and Highway Order 202X and The East Midlands Gateway
Rail Freight and Highway (Amendment) Order 202X

CONTENTS

No.	Item	Page
1.	Introduction	3
2.	Date for submission	3
3.	Statement of Community Consultation	3
4.	Engagement with statutory consultees and stakeholders	3
5.	Project Timeline	4
6.	Tabular Programme	5

EMG2 APPLICATION PROGRAMME

(UPDATED AS AT AUGUST 2025)

1. Introduction

This programme document has been prepared having regard to with the non-statutory guidance published by the Planning Inspectorate (PINS) on the pre-application stage for Nationally Significant Infrastructure Projects as it applies to the standard tier service.

The programme focuses on the pre-application period up to submission and is comprised of two sections. The first section contains a project timeline for the programme representing a simplified summary of the project milestones and events in the preparation of the application. A version of the project timeline has been published by SEGRO (the "Applicant") on its EMG2 webpage since that page went live in November 2024, to keep members of the public and interested parties informed of relevant project milestones. Earlier iterations of this programme document have been provided to and regularly updated for the Planning Inspectorate.

The second section contains a tabular programme which includes additional notes and the identification of the key statutory milestones during the pre-application period which are denoted by ***KM*** in bold. The tabular programme also provides provisional estimated dates for the examination and determination periods based on the anticipated application submission date.

2. Date for Submission of the DCO and MCO Applications

The Applicant intends to submit the DCO and MCO applications simultaneously in **Q3 2025**. This programme has been tailored accordingly and reflects the advanced work and engagement with stakeholders already undertaken.


3. Statement of Community Consultation (SoCC)

The Applicant published the SoCC on 18 December 2024 both on the Applicant's EMG2 webpage and in local newspapers circulating in the vicinity of the site. The SoCC was therefore published well in advance of the 6 week statutory consultation period held between 3 February and 17 March 2025.

4. Engagement with statutory consultees and local authorities

The Applicant has and continues to engage with statutory consultees and has put in place fee funding arrangements with statutory consultees including the Environment Agency and Natural England. In addition, the Applicant has completed a Planning Performance Agreement (PPA) with both North West Leicestershire District Council and Leicestershire County Council. These arrangements further support the Applicant's confidence in securing the engagement it requires during the pre-application period and achieving the timescales in this programme.

Section 1 – Project timeline to submission

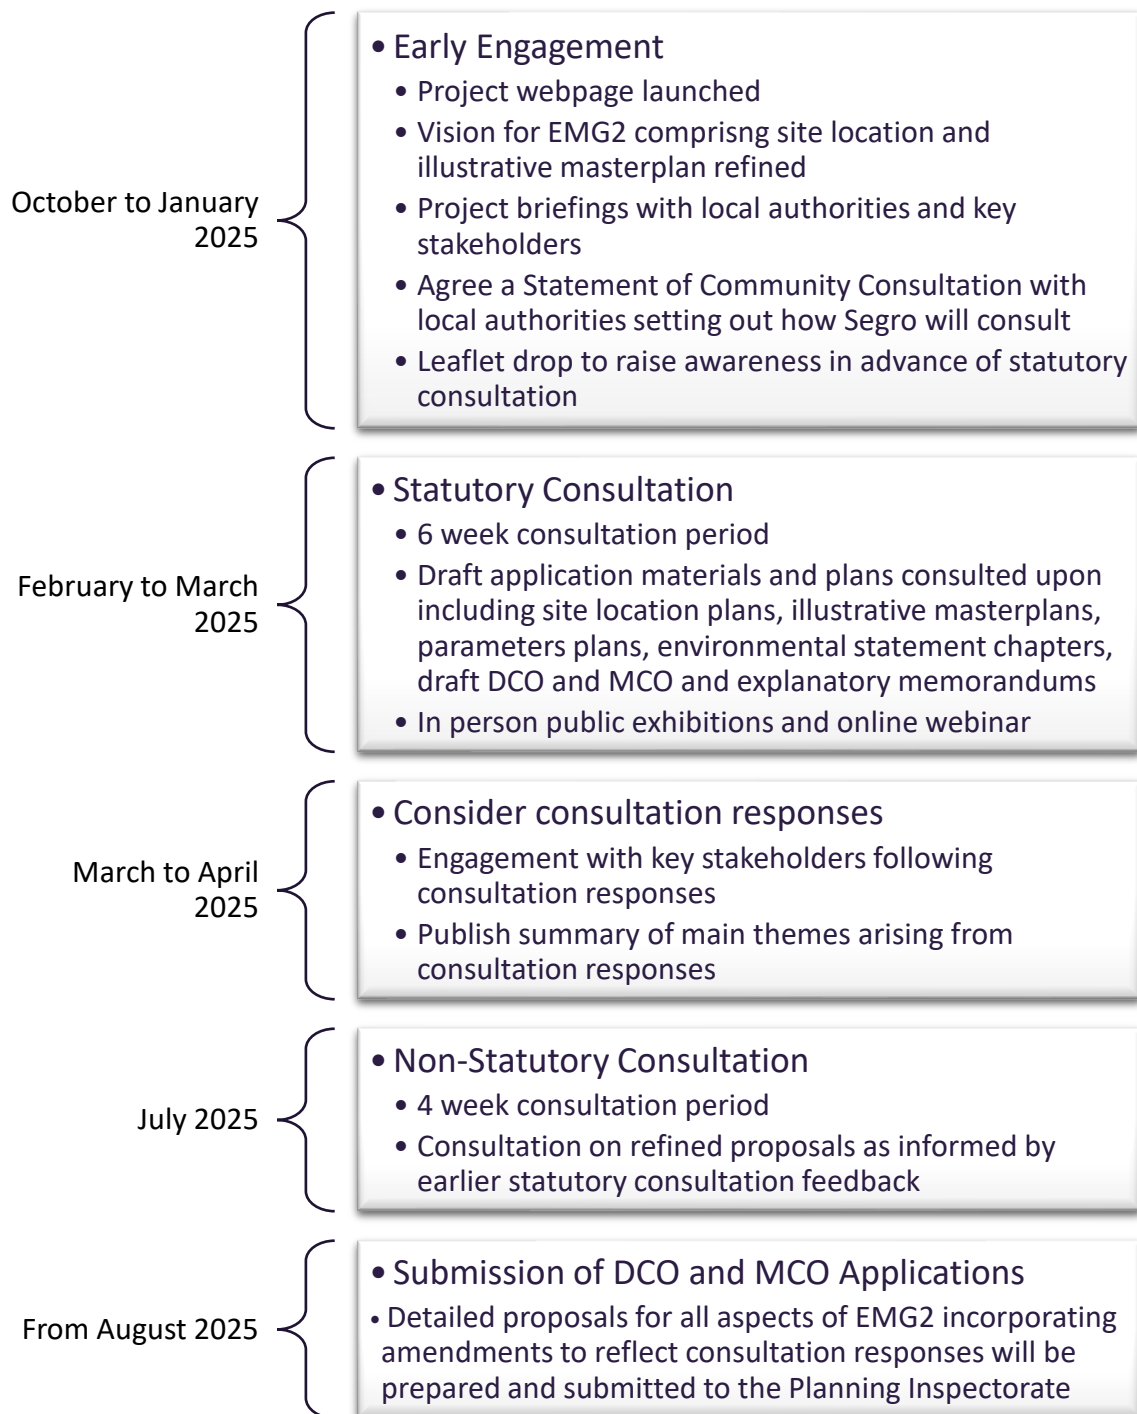

Section 2 – Tabular programme

	KEY STAGE	DATE / PERIOD	NOTES / ASSUMPTIONS
1.	s.35 submission to DLUHC.	22 January 2024	Complete
2.	Decision of DLUHC on s.35 application.	21 February 2024	Complete
3.	Inception meeting with PINS.	13 May 2024	Complete
4.	Instruct land referencers and commence desktop land referencing.	May and June 2024	Complete
5.	Ongoing non-statutory consultation/engagement with key stakeholders and landowners as required.	June to December 2024 and Ongoing as required.	The Applicant is capturing engagement in a consultation log to be included in its Consultation Report.
6.	*KM* Prepare and submit re-scoping request to PINS	August 2024	Complete PINS Scoping Opinion issued 24 September 2024.
7.	Land referencers commence contact referencing to conclude identification of all category 1, 2 and 3 interests.	August 2024 to January 2025	Complete. LIQs prepared and to be sent out in January 2025 prior to statutory consultation.
8.	*KM* Consult with Local Authorities (District and County Council) on Statement of Community Consultation (SOCC).	October 2024	Complete Draft SoCC submitted to LAs in October 2024. LAs responses taken into consideration and revised SoCC published 18 December 2024.
9.	Preparation of document pack for statutory consultation.	November to January 2025	Complete Statutory consultation held 3 February 2025 to 17 March 2025 and included

	KEY STAGE	DATE / PERIOD	NOTES / ASSUMPTIONS
			draft ES chapters (constituting the Preliminary Environmental Information).
10.	*KM* Undertake statutory consultation.	3 February to 17 March 2025	Complete Allowed 6 weeks, more than the minimum 28 days, for responses.
11.	*KM* Submission of draft documentation to PINS.	February 2025	Complete PINS response received 1 April 2025.
12.	*KM* submit Adequacy of Consultation statement to PINS.	28 April 2025	Complete Adequacy of Consultation published on PINS website and SEGRO EMG2 webpage.
13.	Consideration of consultation responses and publication on SEGRO webpage of summary of main themes arising from consultation responses.	March to April 2025	Complete
14.	Refining proposals for EMG2 and preparation of application documentation	Ongoing to June/July 2025	Complete Draft application documentation will be the subject of non-statutory consultation in July 2025
15.	Non-statutory consultation on draft application documentation.	July 2025	Complete 4-week consultation period.
16.	Regular meetings with PINS case officer.	Ongoing submission to	As required. To discuss progress with application

	KEY STAGE	DATE / PERIOD	NOTES / ASSUMPTIONS
			preparation and any issues arising.
17.	*KM* DCO and MCO applications submitted.	From August 2025	Applications to be submitted simultaneously.
18.	Applications accepted for Examination.	TBC (Potentially September 2025)	DCO 28 days after submission. MCO typically 21 days after submission.
19.	Preliminary Meeting and start of Examination.	TBC (Potentially December 2025)	The Secretary(ies) of State may choose to co-join the DCO and MCO applications and examine them together. An examination will be required for the DCO because it involves compulsory purchase powers. However, SEGRO owns all of the MCO land and it is open to the Secretary(ies) of State to determine the MCO application without the need for an examination.
20.	End of Examination.	TBC (Potentially June 2026)	Assumes up to 6 months for examination. DCO examination is up to 6 months. MCO examination is ordinarily 4 months but could be co-joined with the DCO at the discretion of the Secretary(ies) of State.

	KEY STAGE	DATE / PERIOD	NOTES / ASSUMPTIONS
21.	Inspector's Report written and sent to Secretary(ies) of State.	TBC (Potentially September 2026)	DCO 3 months from end of Examination. MCO 2 months from the end of examination, unless co-joined.
22.	Consideration of Inspector's Report and decision by Secretary(ies) of State.	TBC (Potentially December 2026)	DCO 3 months from receipt of Inspector's Report. MCO 2 months from receipt of Inspector's Report, unless co-joined
